)	A	Task Mode	Task Name					Duration	% Complete	Start
0		-5	My Apart	ments Booking				86.75 days?	41%	Thu 8/28/14
1	~	-5	Phase 1					42.5 days?	100%	Thu 8/28/14
2	~	-5	Scope	e				1.25 days	100%	Thu 8/28/14
3	~	-5	De	termine project sco	ope			10 hrs	100%	Thu 8/28/14
4	~	-5	Analy	ysis/Software Requ	irements			11.5 days	100%	Sun 8/31/14
5	~	-5	Re	quirements Elicitat	ion			20 hrs	100%	Sun 8/31/14
6	~	-5	Dr	aft software specifi	cations			20 hrs	100%	Sat 9/13/14
7	~	-5	Re	view software spec	ifications with team			2 hrs	100%	Sat 9/20/14
8	~	-59	Pre	epare software req	uirement specification	ons V1.1		12 hrs	100%	Mon 9/22/14
9	~	-59	Re	view software Requ	uirement specification	ons V1.1 with team		2 hrs	100%	Thu 10/2/14
10	~	-5	Pre	epare software req	uirement specification	ons V1.2		9.5 hrs	100%	Sun 9/28/14
11	~	-5	Re	view software requ	irement specificatio	ns V1.2 with team		2 hrs	100%	Sun 10/12/14
12	~	-5	Pre	epare software req	uirement specification	ons V1.3		2 hrs	100%	Tue 10/14/14
				Task		Inactive Summary		External Task	c	
				Split		Manual Task	-	External Mile		
				Milestone	♦	Duration-only		Deadline	•	
-	-	•	ents Bookin	Summary	<u> </u>	Manual Summary Rollu	р	Progress		
Date:	. FrI 3/	/13/15		Project Summary		Manual Summary		Manual Prog	ress	
				Inactive Task		Start-only	Е			
				Inactive Milestone		Finish-only	3			

D	0	Task Mode	Task Name	Duration	% Complete	Start
13	~	-5	Approve software Requirement specifications V1.3	2 hrs	100%	Thu 10/16/14
14	~	-5	Design	24.25 days?	100%	Mon 10/20/14
15	~	-5	Prepare Functional specifications V1.0	10 hrs?	100%	Mon 10/20/14
16	~	*	Review Functional specifications V1.0 with Team	3 hrs	100%	Thu 10/23/14
17	~	*	Prepare Functional specifications V1.1	47 hrs	100%	Fri 10/24/14
18	~	-5	Review Functional specifications V1.1 with Team	2 hrs?	100%	Thu 10/30/14
19	~	-5	Prepare Functional specifications V1.2	24 hrs?	100%	Fri 10/31/14
20	~	*	Review Functional specifications V1.2 with Team	3 hrs	100%	Thu 11/6/14
21	~	-5	Prepare Functional specifications V1.3	46 hrs?	100%	Fri 11/7/14
22	~	*	Review Functional specifications V1.3 with Team	3 hrs	100%	Thu 11/20/14
23	~	*	Obtain approval to proceed	1 hr	100%	Thu 11/20/14
24	~	-5	Incorporate feedback into functional specifications	30 hrs?	100%	Fri 11/21/14
25	✓	-5	Obtain approval to proceed	1 hr?	100%	Thu 11/27/14

External Tasks Task Inactive Summary Split Manual Task External Milestone Milestone Duration-only Deadline Project: My Apartments Bookin Manual Summary Rollup Summary Progress Date: Fri 3/13/15 Manual Summary **Project Summary** Manual Progress Inactive Task Start-only Е Finish-only J Inactive Milestone

D	0	Task Mode	Task Name					Duration	% Comple	ete Start
26	V		Ris	sk Management Plan				22 hrs?	100%	Fri 11/28/14
27	~	-5	Qu	iality Assurance Plan				30 hrs?	100%	Fri 12/5/14
28	√	-5	Othe	r Changes				30 hrs?	100%	Fri 12/12/14
29		*	Phase 2					28.38 days	s 15%	Tue 2/24/15
30		-5	Admi	in Side				18 days	19%	Tue 2/24/15
31	✓	*	Log	gin Page				16 hrs	100%	Tue 2/24/15
32	~	*	Ve	ndor Request				12 hrs	100%	Sat 2/28/15
33		*	Ad	min Management				10 days	44%	Mon 3/2/15
34	~	*		Users				24 hrs	100%	Mon 3/2/15
35	✓	*		User Groups				16 hrs	100%	Mon 3/2/15
36	~	*		User Property				24 hrs	100%	Thu 3/5/15
37	~	-5	,	Vendor Request				16 hrs?	100%	Tue 3/3/15
38		-5		Email Templates				12 hrs?	0%	Sat 3/14/15
39		-5		Application Errors				24 hrs?	0%	Sat 3/14/15
				Task		Inactive Summary	n	External	Tacks	
				Split		Manual Task	u u			♦
				Milestone	♦	Duration-only		Deadlin		* ↓
-	•	•	ents Bookin	Summary		Manual Summary Roll	up	Progres		
Date:	Fri 3/	13/15		Project Summary		Manual Summary		_	Progress	
				Inactive Task		Start-only	Е		-	
						Finish-only				


D	0	Task Mode	Task Name					Duration	% Complete	Start
40	Ĭ			Set Banner				16 hrs?	0%	Tue 3/17/15
41		-5	,	Website CMS				16 hrs?	0%	Sat 3/21/15
42		-5	,	Website Links				16 hrs?	0%	Tue 3/17/15
43		-5		Posted Reviews & C	Comments			16 hrs?	0%	Tue 3/24/15
44		*	Pro	operty Setting				5.75 days	0%	Tue 3/24/15
45	i	-5		City Managment				14 hrs?	0%	Tue 3/24/15
46	i	-5		Town Management				12 hrs?	0%	Tue 3/24/15
47		-5		Facility Managemer	nt			14 hrs?	0%	Tue 3/24/15
48		-5		Facility Profile				16 hrs?	0%	Tue 3/31/15
49		-5		Policy Profile				12 hrs?	0%	Tue 3/31/15
50		-5		Property Categories	3			15 hrs?	0%	Tue 3/31/15
51		-5		Base Comission				14 hrs?	0%	Tue 3/31/15
52		*	Pro	operty Managment				5.75 days	0%	Tue 4/7/15
53		-5		Property List				16 hrs?	0%	Tue 4/7/15
							П		1	
				Task Split		Inactive Summary Manual Task	U	External External	Milestone \diamondsuit	
				Milestone	♦	Duration-only		Deadline		
-	-	•	ents Bookin	Summary		Manual Summary Roll	up	Progress		
Date:	Fri 3/1	13/15		Project Summary		Manual Summary		Manual		
				Inactive Task		Start-only	Е			


D	0	Task Mode	Task Name					Duration	% Complete	Start
54		*		Property Facilities				16 hrs?	0%	Tue 4/7/15
55		-5		Property Policy				16 hrs?	0%	Tue 4/7/15
56		4		Property Graphics				24 hrs?	0%	Tue 4/7/15
57	ŧ	*		Property Promotion	ns			16 hrs?	0%	Tue 4/14/15
58	ŧ	*		Featured Property				16 hrs?	0%	Tue 4/14/15
59	ŧ	*		Property of Month				16 hrs?	0%	Wed 4/15/15
60	ŧ	*		Property Comission	1			8 hrs?	0%	Sat 4/18/15
61		*		Property Calender				8 hrs?	0%	Sun 4/19/15
62		*		Property Approved,	/UnApproved List			15 hrs?	0%	Sat 4/18/15
63		*		ports				2.13 days	0%	Sat 4/18/15
64	i	*		Booking Income Re	port			14 hrs?	0%	Sat 4/18/15
65	ŧ	*		Vendor Property Lis	st Report			17 hrs?	0%	Tue 4/21/15
66	ŧ	*		Booking Comission	Report			17 hrs?	0%	Tue 4/21/15
67		*	Pro	operty Booking				3.5 days	0%	Thu 4/23/15
68	ŧ			Booking History				12 hrs?	0%	Thu 4/23/15
				Task		Inactive Summary		External T	asks	
				Split		Manual Task		External N		
				Milestone	♦	Duration-only		Deadline	•	
-	-		ents Bookin	Summary		Manual Summary Rol	lup	Progress		
Date:	: Fri 3,	/13/15		Project Summary		Manual Summary		Manual Pi	ogress	
				Inactive Task		Start-only	Е		-	
				Inactive Milestone		Finish-only	3			


)	0	Task Mode	Task Name					Duration	% Complete	Start
69		-5		Search booking				12 hrs?	0%	Thu 4/23/15
70	İ			Change Booking				12 hrs?	0%	Thu 4/23/15
71				Create Booking				12 hrs?	0%	Thu 4/23/15
72	ŧ	*		Update Customer d	letails			9 hrs?	0%	Tue 4/28/15
73		*	Clien	t Side				4.75 days	0%	Thu 4/30/15
74		*	Но	me Page				22 hrs	0%	Thu 4/30/15
75	Ť	*		Search Apartment +	+ Hot Deals			22 hrs?	0%	Thu 4/30/15
76		*	Ар	artment Full List Pa	age			28 hrs	0%	Thu 4/30/15
77	i	*		Booking & Payment	t			28 hrs?	0%	Thu 4/30/15
78			My	/ Bookings				12 hrs?	0%	Thu 4/30/15
79		-	Vie	ewed Apartments				12 hrs?	0%	Thu 4/30/15
80	III	-5	Ma	ар				10 hrs?	0%	Tue 5/5/15
81		-5	Em	nail Enquiry				10 hrs?	0%	Tue 5/5/15
82		-5	FA	Q'S				8 hrs?	0%	Tue 5/5/15
83		-5	Co	ntact US				8 hrs?	0%	Tue 5/5/15
84		*	Testi	ng				2.13 days	0%	Sun 5/10/15
				Task		Inactive Summary		External T	asks	
				Split		Manual Task		External N	Milestone ♦	
				Milestone	♦	Duration-only		Deadline	•	
-	-	•	nts Bookin	Summary		Manual Summary Roll	lup	Progress		
Jate:	rfi 3/	13/15		Project Summary		Manual Summary		Manual Pr	rogress	
				Inactive Task		Start-only	Е			

.D		Task	Task Name	Duration	% Complete	Start
	U	Mode				
85		*	Application Testing	2.13 days	0%	Sun 5/10/15
86		*	Bug Fixing	4 days	0%	Tue 5/12/15
87		*	Application Issue Fixing	4 days	0%	Tue 5/12/15
88		-5	Other Changes	3 days?	0%	Sun 5/10/15

Inactive Summary External Tasks Task Split Manual Task External Milestone \Diamond Milestone Duration-only Deadline Project: My Apartments Bookin Manual Summary Rollup Progress Summary Date: Fri 3/13/15 Manual Summary **Project Summary** Manual Progress Inactive Task Start-only Е Finish-only J Inactive Milestone Page 7

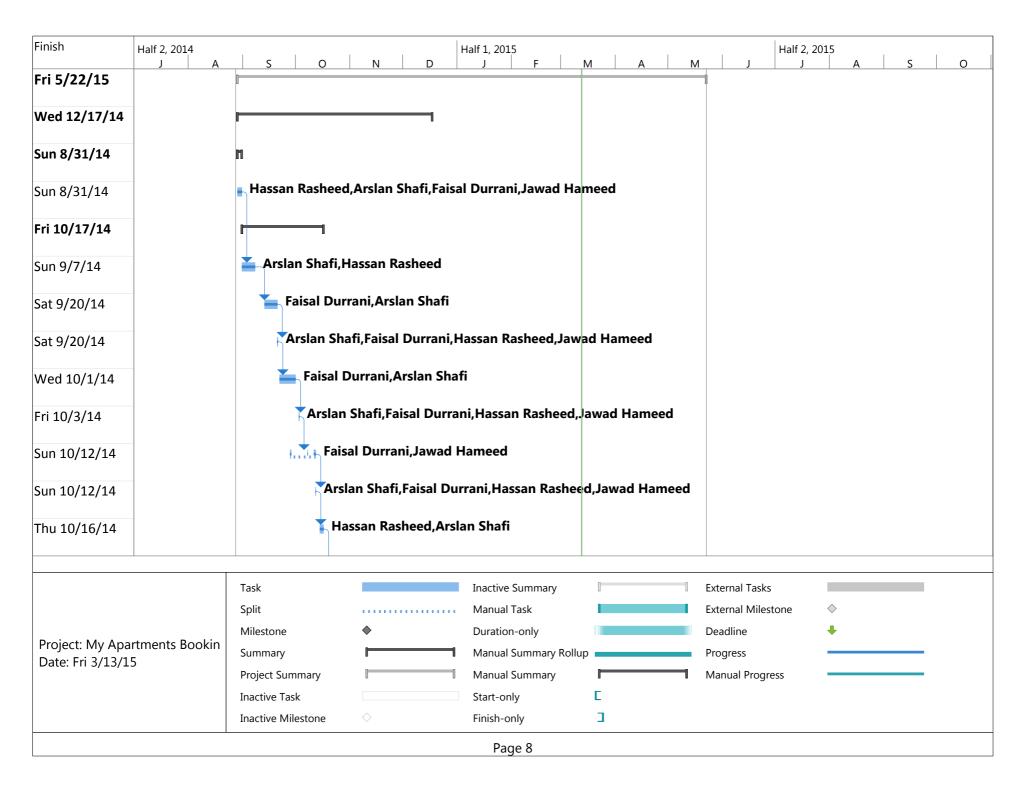

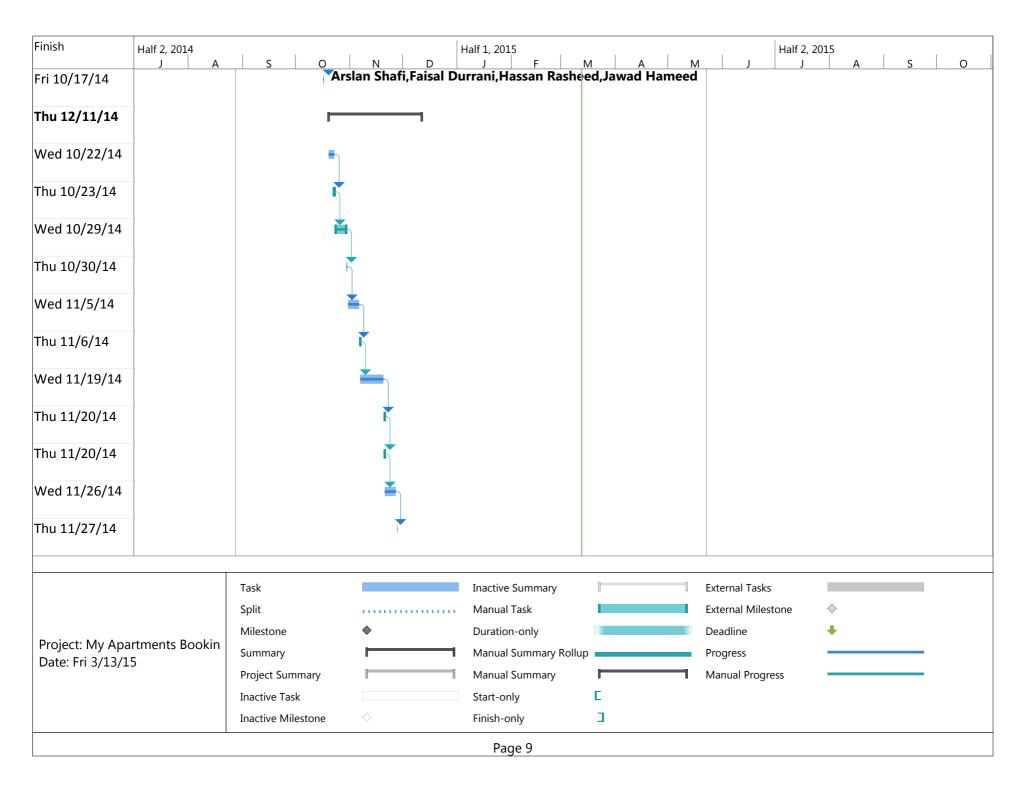

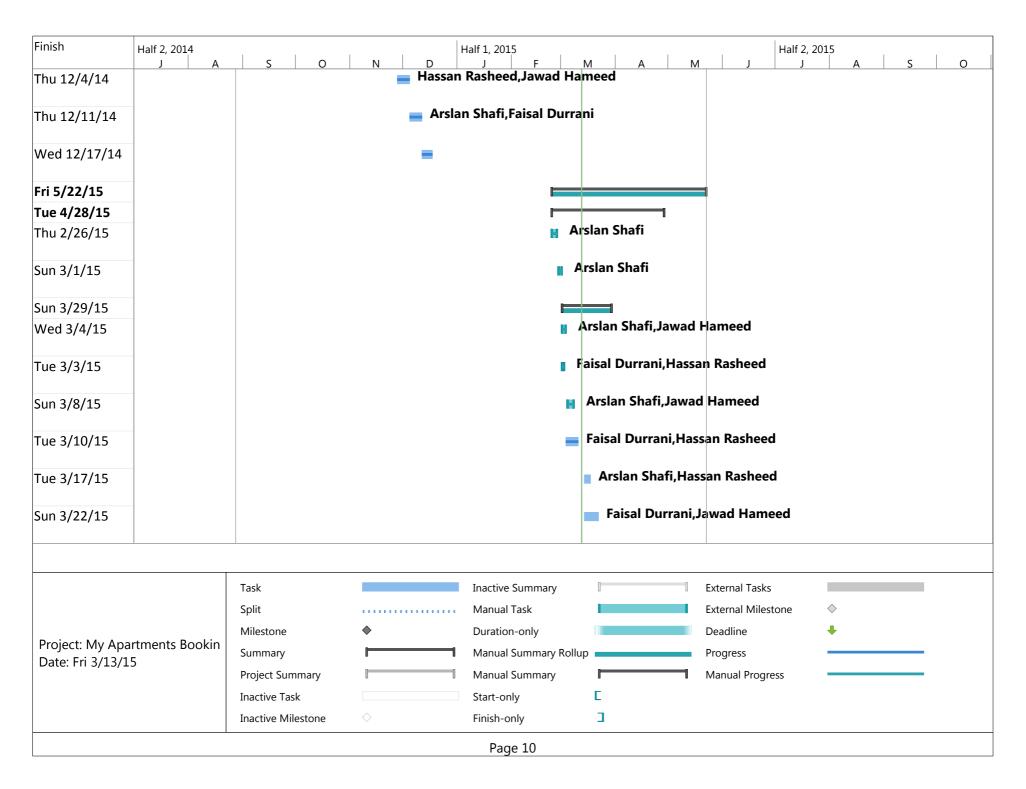

Finish	Half 2, 2014	1 1		Half 1, 2015		1	Half 2, 20		1 1	
Sun 3/22/15	J	A S O	N D	J F N	A Arslan Shafi	M J	<u> </u>	A	S	0
Fri 3/27/15					Faisal Durr	ani,Jawad Han	need			
FII 3/2//13										
Sun 3/22/15					Hassan Rash	need				
Sun 3/29/15					Arslan Sha	afi				
Sun 4/5/15										
Sun 3/29/15					Faisal Dur	rani				
Sun 3/29/15					Jawad Hai	meed				
Sun 3/29/15					Hassan Ra	sheed				
Sun 4/5/15					Arslan S	Shafi				
Sun 4/5/15					Hassan l	Rasheed				
Sun 4/5/15					Jawad F	lameed				
Sun 4/5/15					Faisal D	urrani				
Tue 4/21/15										
Sun 4/12/15					Hassa	n Rasheed				
		Task		Inactive Summary		External Tasks		^		
		Split		Manual Task		External Miles	tone	♦		
Project: My Ap	artments Book	Milestone kin	♦	Duration-only		Deadline		•		
Date: Fri 3/13/		Summary		Manual Summary Rollup		Progress				
		Project Summary		Manual Summary		Manual Progr	ess			
		Inactive Task		Start-only	С					
		Inactive Milestone		Finish-only]					

Finish	Half 2, 2014						Half 1, 2015							Half 2,	2015			
	J	Α	S	0	N	D	J	F	M	Α		M	J	J		\	S	0
Sun 4/12/15												Hame						
Sun 4/12/15										F	aisal I	Durran	ni					
Sat 4/18/15											Arsla	n Shaf	fi					
Wed 4/15/15										•	Jawa	d Ham	eed					
Wed 4/15/15											Faisal	Durra	ni					
Thu 4/16/15										•	Hassa	an Ras	heed					
Sat 4/18/15										•	Faisa	al Duri	rani					
Sun 4/19/15										•	Arsl	an Sha	afi					
Tue 4/21/15											Has	san Ra	asheed					
Thu 4/23/15																		
Sun 4/19/15										ı	Jaw	ad Hai	meed					
Thu 4/23/15											∏ Fai	sal Du	rrani					
Thu 4/23/15											J av	vad Ha	ameed					
Tue 4/28/15																		
Sun 4/26/15											■ Fai	sal Du	rrani					
		1	Гask				Inactive S	ummary				Exte	ernal Task	S				
		5	Split				Manual T	ask				Exte	ernal Mile	stone	\Diamond			
5		. 1	Milestone		♦		Duration-	only				Dea	dline		•			
Project: My Apar Date: Fri 3/13/15		an s	Summary				Manual S	ummary Ro	ollup 📥			Prog	gress					
Date. 111 3/13/13	,	F	Project Sum	mary			Manual S	ummary				I Mar	nual Prog	ress				
		I	nactive Tasl	<			Start-only	/	Е									
		I	nactive Mile	estone	\Diamond		Finish-on	ly	3									
		•					Page	12										

Finish	Half 2, 2014						Half 1, 201	5 .					Half 2, 2	2015		
	J	Α	S	0	N	D	J	F	М	Α	M	J Deels end	l j	A	 S	0
Sun 4/26/15											Hassar	n Rasheed				
Sun 4/26/15											Jawad	Hameed				
Sun 4/26/15											Arslan	Shafi				
Tue 4/28/15											Arsla	n Shafi				
Sat 5/9/15																
Sat 5/2/15											H					
Sat 5/2/15											Arsl	an Shafi				
Sun 5/3/15											H					
Sun 5/3/15											■ Has	san Rashe	ed			
Sun 5/3/15											Jawa	ad Hamee	d			
Sun 5/3/15											■ Faisa	al Durrani				
Sat 5/9/15											Ar:	slan Shafi				
Sat 5/9/15											Jav	wad Hame	ed			
Sat 5/9/15											■ Ha	ssan Rash	eed			
Sat 5/9/15											Fai	isal Durraı	ni			
Sat 5/16/15																
			Task				Inactive :	Summary				External Task	S			
			Split				• Manual 1	Гask				External Mile	stone	\Diamond		
		_	Milestone		♦		Duration	i-only				Deadline		•		
Project: My Apa Date: Fri 3/13/1		okin	Summary				1 Manual S	Summary Ro	ollup 🚃			Progress				
Date. 111 3/13/1	J		Project Sumn	nary			1 Manual S	Summary				Manual Prog	ess			
			Inactive Task				Start-on	ly	Е							
			Inactive Mile	stone	\Diamond		Finish-or	nly	3						 	
				· · · · · ·			Page	e 13	· · · · · ·	· · · · · ·			· · · · ·		 	

